



BOARD UPDATE

WILLIAM J. CLARK MIDDLE SCHOOL





WILLIAM J. CLARK MIDDLE SCHOOL

IN THE LAST FEW WEEKS, WE HAVE:

- Completed the building pad on 9/4
- Plumber began interior sewer and new acid dilution waste line on 9/18
- Footings began on 9/25

LOOK AHEAD:

- Pouring footings 10/3 (40%). Will look to complete footers week of 10/16
- Block mason to begin foundation block 10/16
- Electrician to begin running Underground conduit on 10/9
- Plumber continue interior sewer work. Finishing week of 10/25

**- NO SAFETY OR SECURITY
ISSUES -**

WILLIAM J. CLARK MIDDLE



WILLIAM J. CLARK MIDDLE



WILLIAM J. CLARK MIDDLE



WILLIAM J. CLARK MIDDLE



WILLIAM J. CLARK MIDDLE



WILLIAM J. CLARK MIDDLE



WILLIAM J. CLARK MIDDLE





BOARD UPDATE

LAKE MARION MIDDLE SCHOOL



PROGRESS UPDATE



LAKE MARION MIDDLE SCHOOL

IN THE LAST FEW WEEKS, WE HAVE:

- Completed the building pad week of 9/22
- Footings began on 9/25. We are currently 30% complete with footers.

LOOK AHEAD:

- Looking to complete footers by 10/9
- Electrician began running underground electrical conduit
- Plumber to begin interior sewer 10/9
- Block Mason to begin foundation 10/9

- NO SAFETY OR SECURITY ISSUES -

LAKE MARION MIDDLE



LAKE MARION MIDDLE



LAKE MARION MIDDLE



LAKE MARION MIDDLE



LAKE MARION MIDDLE



LAKE MARION MIDDLE



OCSD – East Elementary

WEEK OF October 6th, 2023



	SAFETY	
	Incidents to Date	0
	First Aids to Date	0

	SCHEDULE MILESTONES	
	• Installation of temporary construction fence.	
	• Temporary bus loop.	

	WEATHER	
	Working Days	5
	Weather Days	0
	Activities Delayed	0

	MANPOWER	
	Number of Trades	2
	Average Workers (per day)	10

TOP ACTIVITIES THIS WEEK

- Installed and passed inspection of the temporary bus loop.
- Installed construction fencing
- Continued development of building pads C & B

UPCOMING ACTIVITIES

- Pond excavation
- Continue with the building pads for area C & B
- Subcontractor Kickoff Meeting 10/11 at 9AM
- OAC Meeting #2 10/12 at 1PM






ORANGEBURG COUNTY SCHOOL DISTRICT

BOARD PRESENTATION

OCTOBER 10, 2023

LS3P

DESIGN PROCESS – ORANGEBURG-WILKINSON HIGH SCHOOL

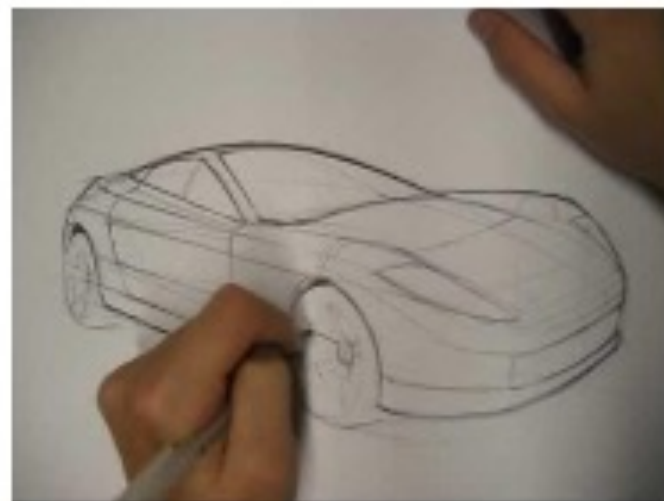

ORANGEBURG-WILKINSON HIGH SCHOOL



DESIGN DEVELOPMENT SITE PLAN: COOK RD.
ORANGEBURG COUNTY SCHOOLS PROJECT UPDATES



ORANGEBURG-WILKINSON HIGH SCHOOL



1st Floor Plan

COLORED LEGEND

- ADMINISTRATION
- AUDITORIUM
- CLASSROOMS - ACADEMIC
- CORE
- CORRIDOR
- PE / GYM
- RESOURCE/SPECIAL NEEDS
- RESTROOM
- SCIENCE
- SUPPORT
- SUPPORT CLASS



1,300 Students
(1,600 Students Core/Future Expansion)

Main Building

1st Floor Area: 191,506 SF

2nd Floor Area: 88,703 SF

Total Area: 280,209 SF

Baseball/Softball Support Building Area:

2,195 SF

Field House Building Area: 15,411 SF

Press Box Building Area: 687 SF

Total Area: 18,293 SF

Total Square Footage: 298,502 SF

ORANGEBURG-WILKINSON HIGH SCHOOL



2nd Floor Plan

COLORED LEGEND

- ADMINISTRATION
- AUDITORIUM
- CLASSROOMS - ACADEMIC
- CORE
- CORRIDOR
- PE / GYM
- RESOURCE/SPECIAL NEEDS
- RESTROOM
- SCIENCE
- SUPPORT
- SUPPORT CLASS



1,300 Students
(1,600 Students Core/Future Expansion)

Main Building


1 st Floor Area:	191,506 SF
2 nd Floor Area:	88,703 SF
Total Area:	280,209 SF
Baseball/Softball Support Building Area:	2,195 SF
Field House Building Area:	15,411 SF
Press Box Building Area:	687 SF
Total Area:	18,293 SF
Total Square Footage:	298,502 SF



ORANGEBURG-WILKINSON HIGH SCHOOL



Field House


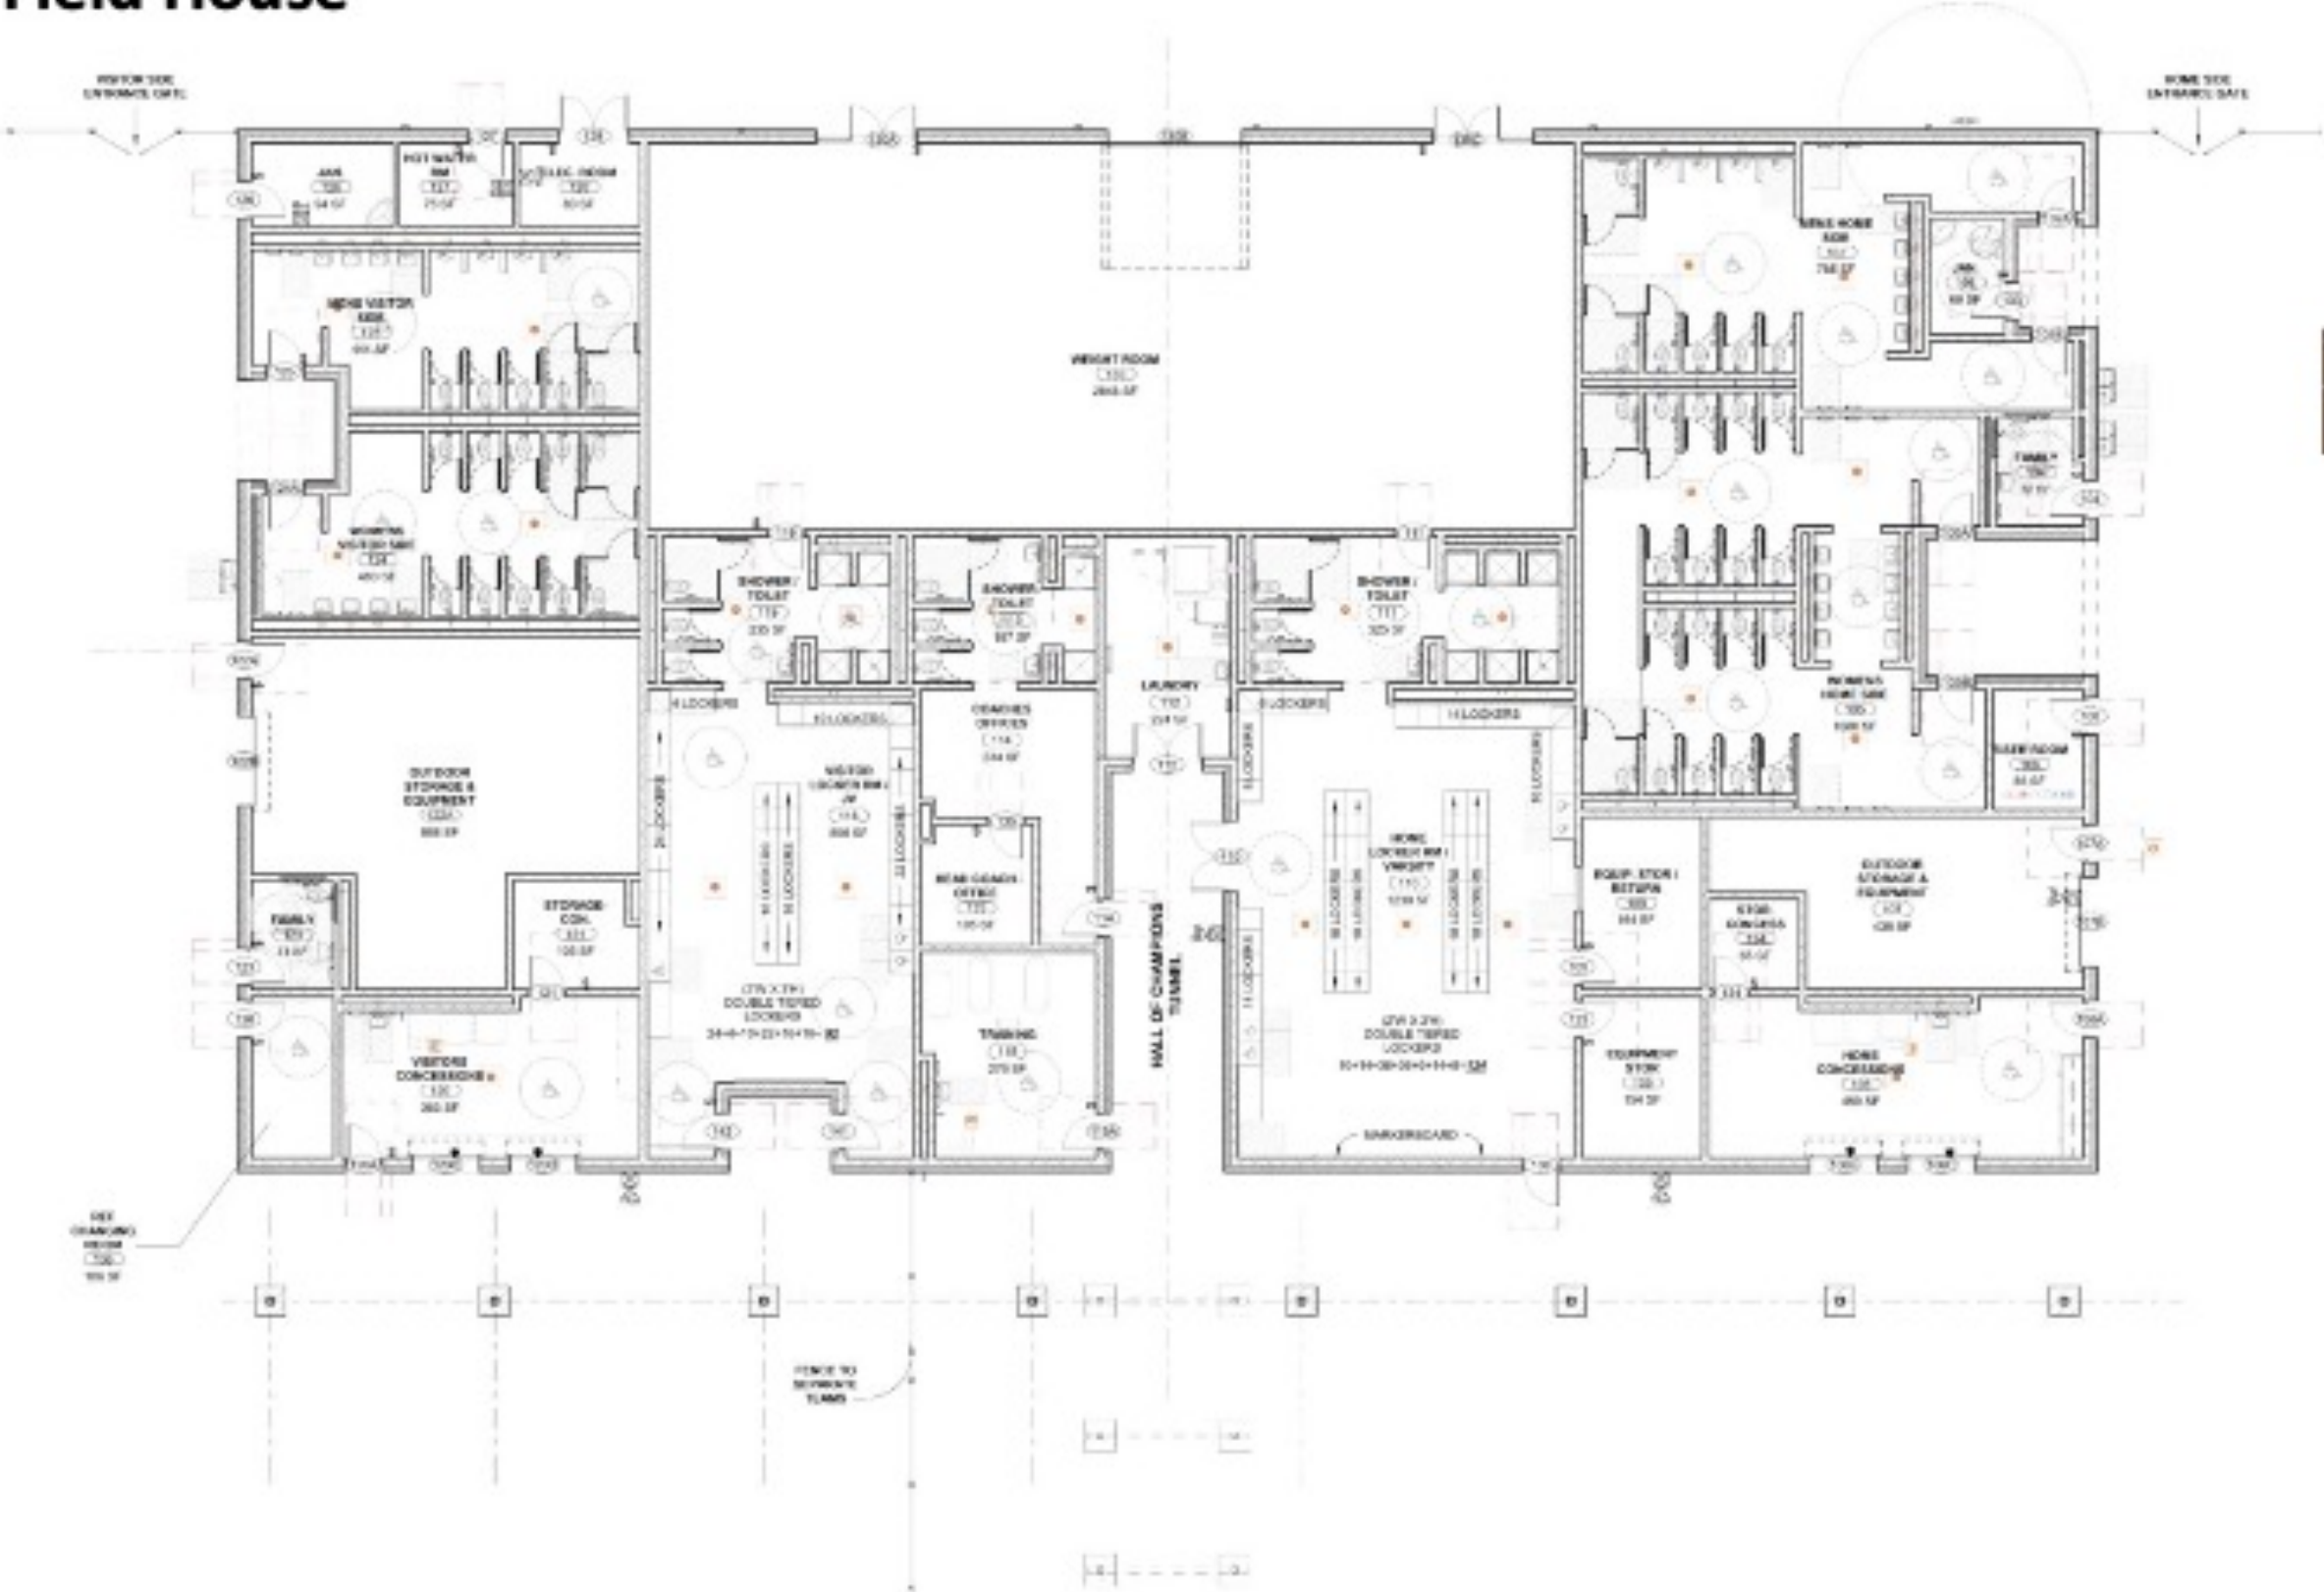


1,300 Students	
(1,600 Students Core/Future Expansion)	
<u>Main Building</u>	
1 st Floor Area:	191,506 SF
2nd Floor Area:	88,703 SF
Total Area:	280,209 SF
<u>Baseball/Softball Support Building Area:</u>	
	2,195 SF
Field House Building Area:	15,411 SF
Press Box Building Area:	687 SF
Total Area:	18,293 SF
Total Square Footage:	298,502 SF



ORANGEBURG-WILKINSON HIGH SCHOOL


Baseball/Softball Support

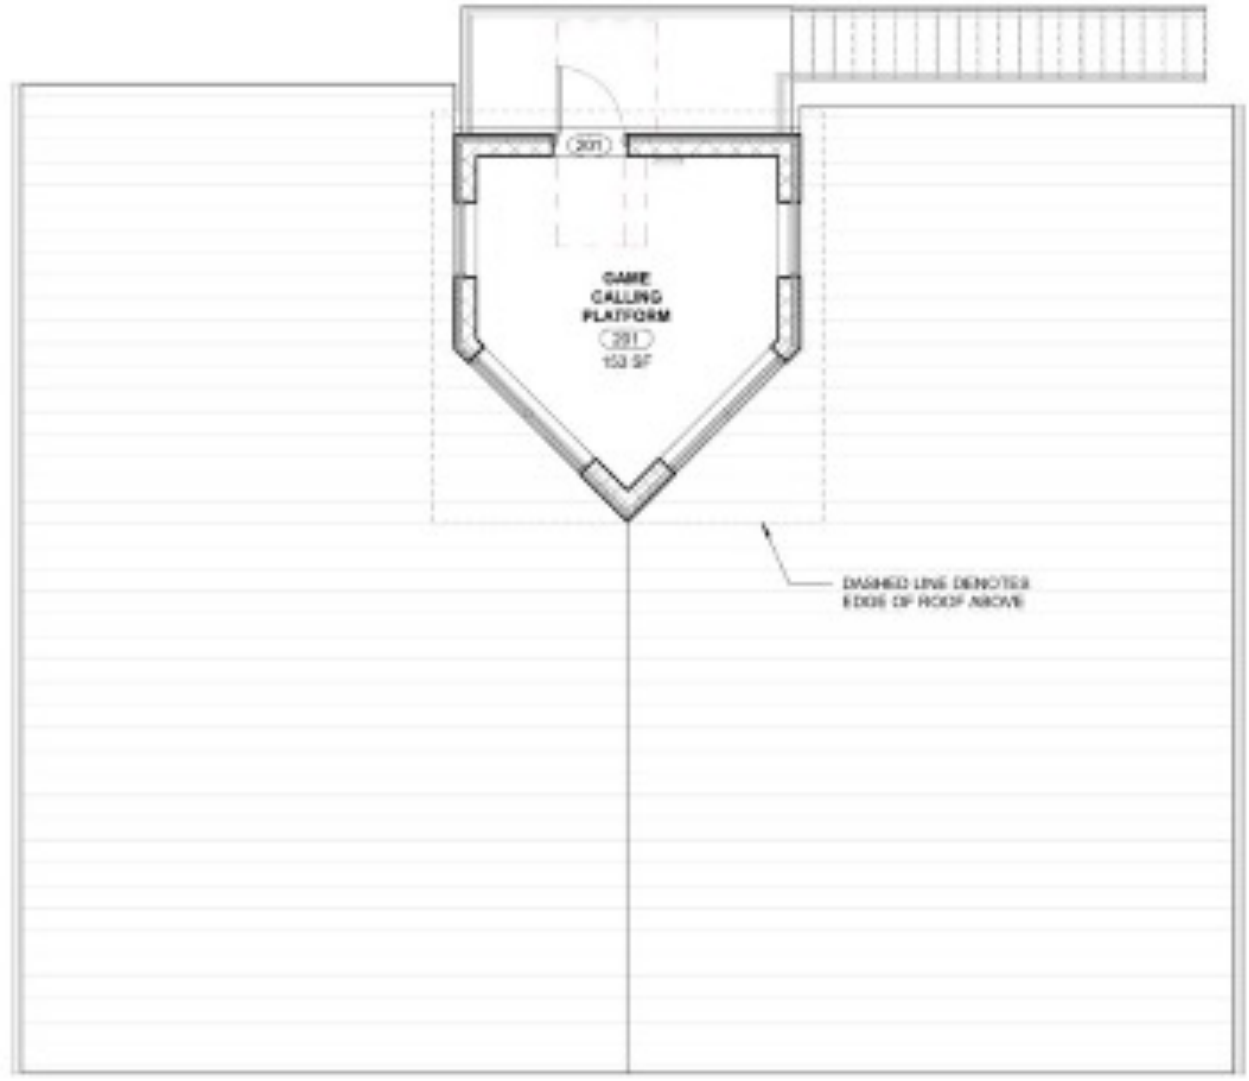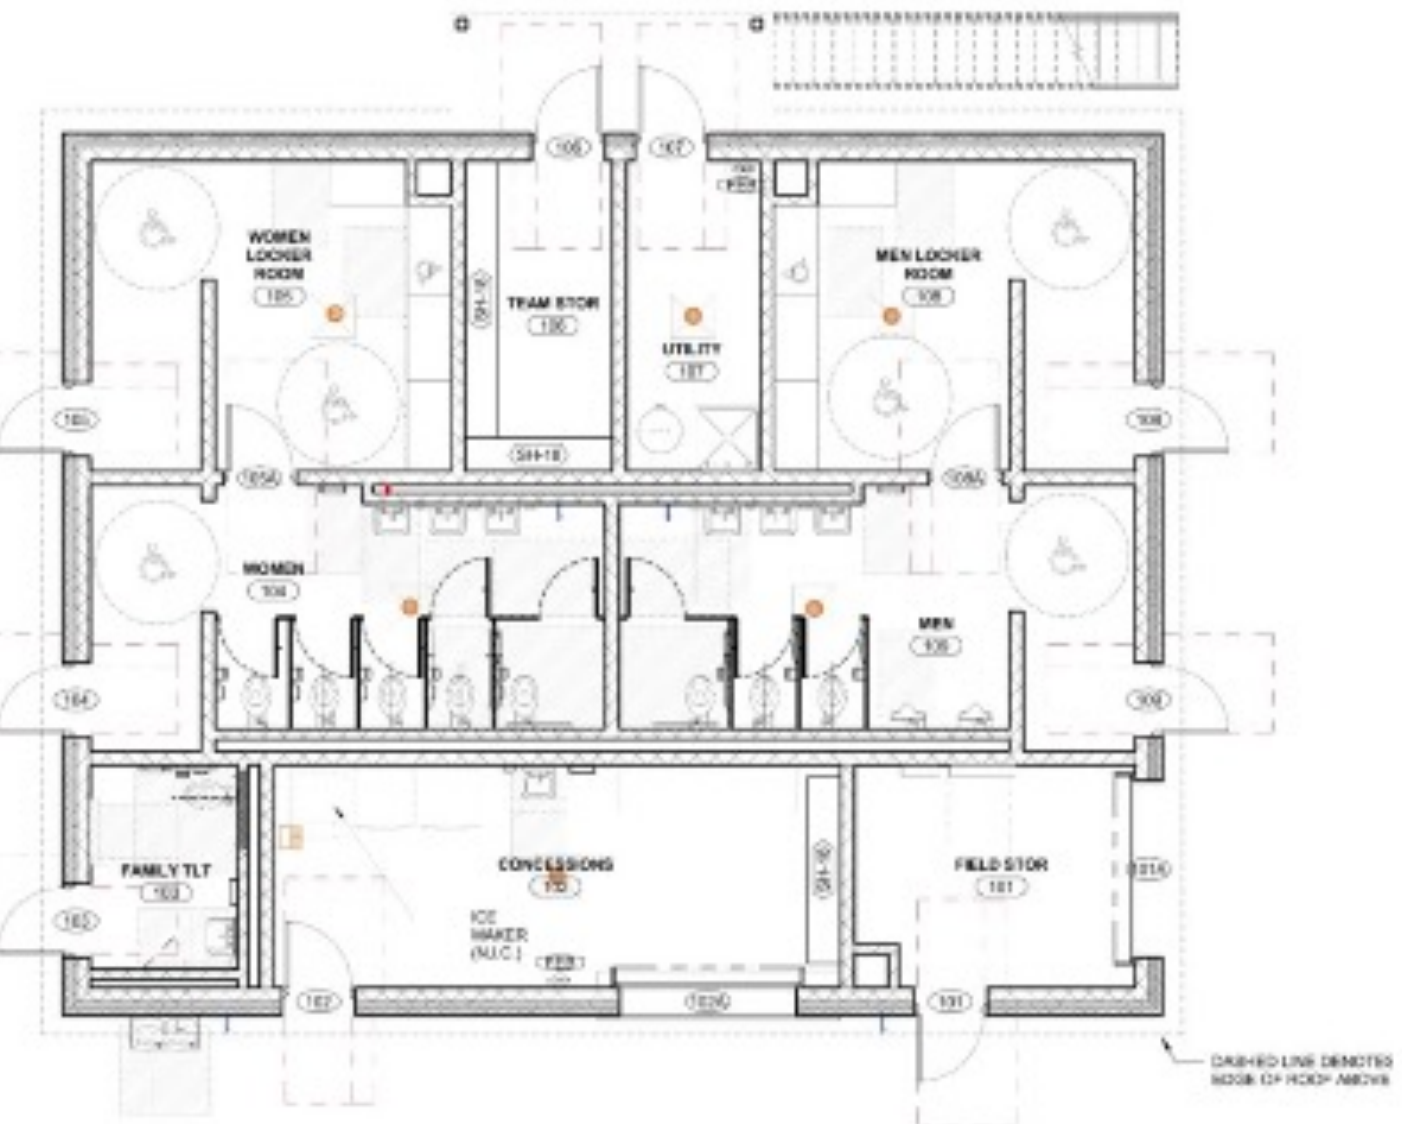

1,300 Students	
(1,600 Students Core/Future Expansion)	
Main Building	
1 st Floor Area:	191,506 SF
2nd Floor Area:	88,703 SF
Total Area:	280,209 SF
Baseball/Softball Support Building Area:	
	2,195 SF
Field House Building Area:	15,411 SF
Press Box Building Area:	687 SF
Total Area:	18,293 SF
Total Square Footage:	298,502 SF

ORANGEBURG-WILKINSON HIGH SCHOOL

Press Box

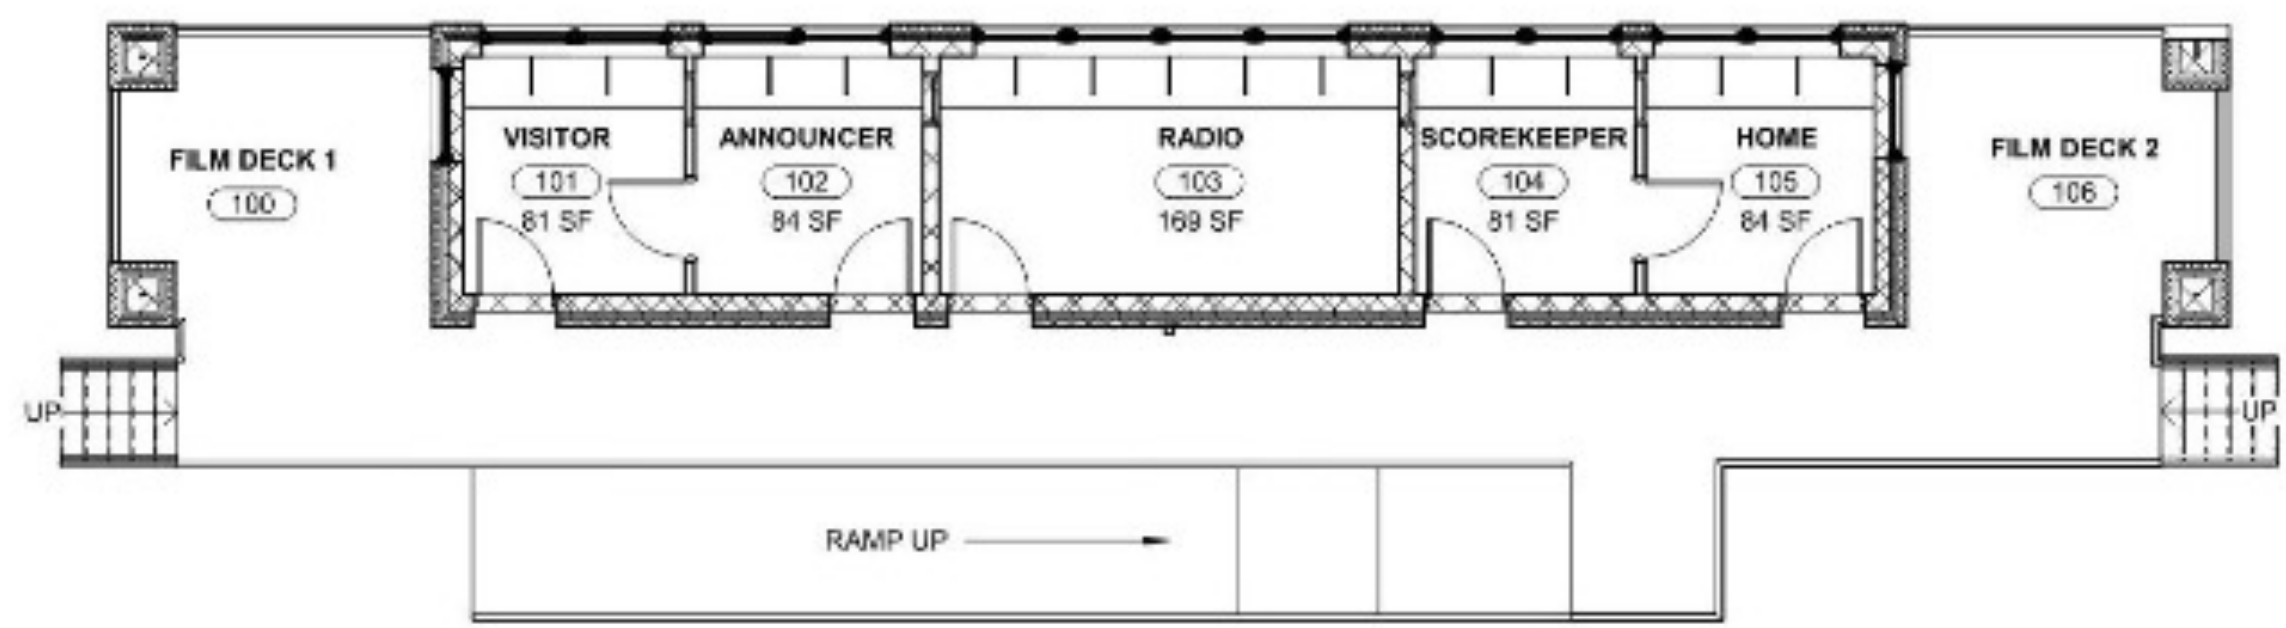

1,300 Students	
(1,600 Students Core/Future Expansion)	
Main Building	
1 st Floor Area:	191,506 SF
2nd Floor Area:	88,703 SF
Total Area:	280,209 SF
Baseball/Softball Support Building Area:	
	2,195 SF
Field House Building Area:	15,411 SF
Press Box Building Area:	687 SF
Total Area:	18,293 SF
Total Square Footage:	
	298,502 SF

ORANGEBURG-WILKINSON HIGH SCHOOL



ORANGEBURG-WILKINSON HIGH SCHOOL



ORANGEBURG-WILKINSON HIGH SCHOOL



ORANGEBURG-WILKINSON HIGH SCHOOL



ORANGEBURG-WILKINSON HIGH SCHOOL



ORANGEBURG-WILKINSON HIGH SCHOOL



ORANGEBURG-WILKINSON HIGH SCHOOL



ORANGEBURG-WILKINSON HIGH SCHOOL



ORANGEBURG-WILKINSON HIGH SCHOOL



ORANGEBURG-WILKINSON HIGH SCHOOL



ORANGEBURG-WILKINSON HIGH SCHOOL


ORANGEBURG-WILKINSON HIGH SCHOOL	COSTS		DESIGN DEVELOPMENT ESTIMATE	SCHEMATIC DESIGN ESTIMATE	NOTES
DESCRIPTION	GSF	\$/GSF			
ESTIMATED CONSTRUCTION COSTS					
SITE					
Site Development			\$ 18,375,360.00	\$ 14,366,104.00	Grading, erosion control, paving and utilities
Site Athletics			\$ 9,813,916.00	\$ 10,967,893.00	Fields, Stadium, Press Box
Off-site Development			\$ 1,613,246.00	\$ 1,111,430.00	Turn lanes and utilities
Site Sub-total			\$ 29,802,522.00	\$ 26,445,427.00	
BUILDING					
Building- New Construction High School	280,209	\$ 288.06	\$ 80,716,267.00	\$ 80,468,330.00	
Building- New Construction Athletics	17,606	\$ 388.52	\$ 6,840,298.00	\$ 8,785,243.00	Field House, Baseball/Softball Building
Building Sub-total			\$ 87,556,565.00	\$ 89,253,573.00	
Site & Building Sub-total			\$117,359,087.00	\$ 115,699,000.00	Precon/estimating, construction and fees
Contingencies			\$ 8,245,058.00	\$ 9,596,000.00	% of Site & Building Sub-total
ESTIMATED TOTAL CONSTRUCTION COSTS *		\$ 450.80	\$125,604,145.00	\$ 125,295,000.00	+ Owner soft costs TBD = <u>Total Project Cost</u>

NOTE: * This Construction Cost Estimate is a summary based on M.B. Kahn's estimate of the Design Development of Orangeburg-Wilkinson High School

ORANGEBURG-WILKINSON HIGH SCHOOL



ORANGEBURG-WILKINSON HIGH SCHOOL

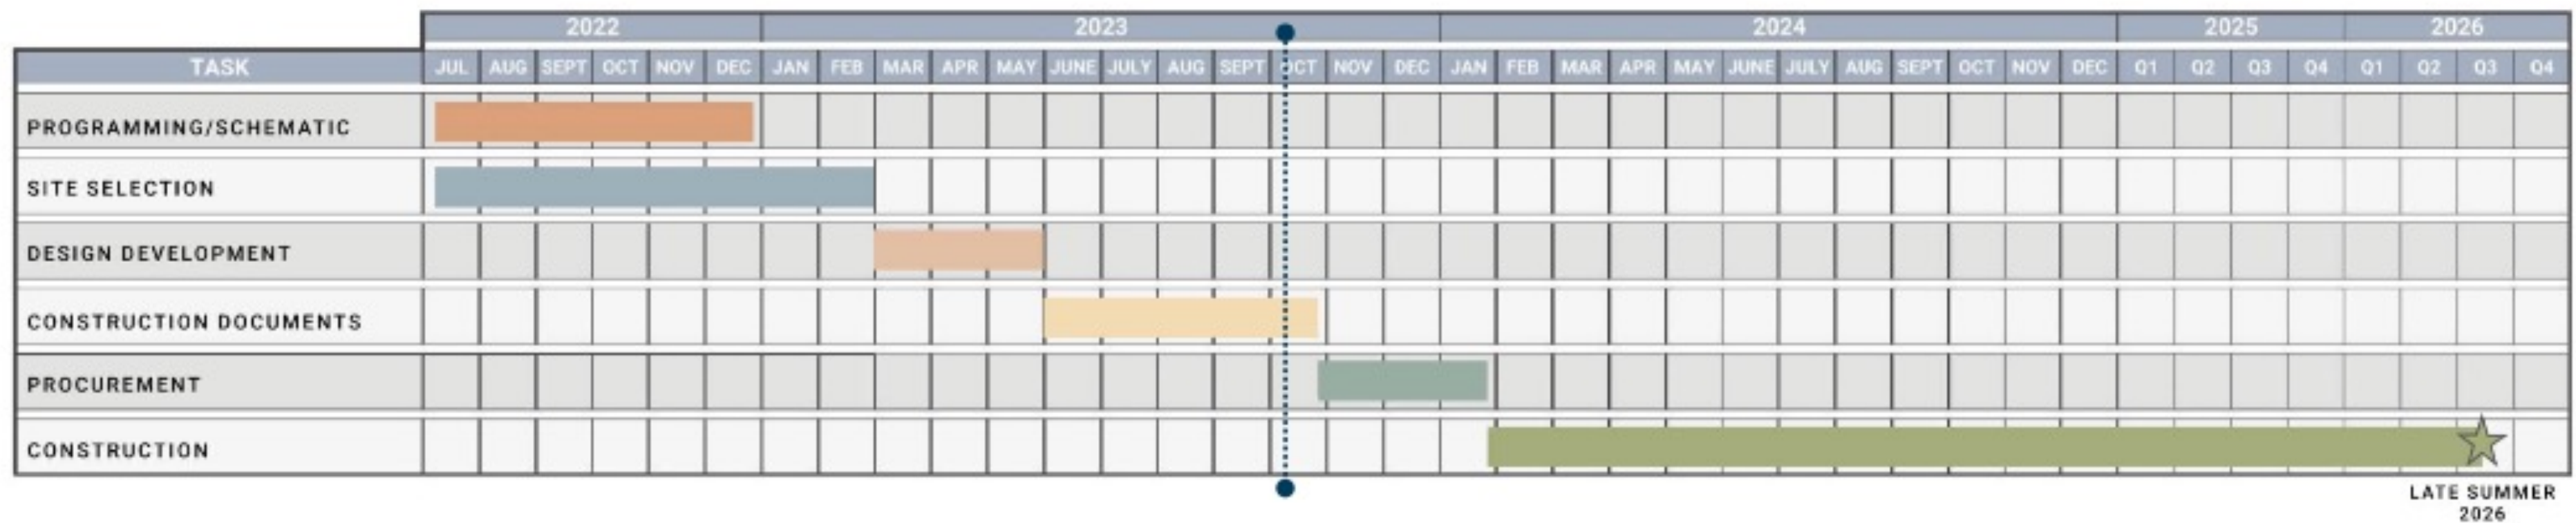

ORANGEBURG-WILKINSON HIGH SCHOOL	
DESIGN (PROGRAMMING - CD'S)	15 MONTHS (JULY 2022 - OCTOBER 2023)
BIDDING/CONSTRUCTION	30 MONTHS (FEBRUARY 2023 - LATE SUMMER 2026)





QUESTIONS?



Reconstructing THE FUTURE



THE HARD RESET




DIGITAL SCOREBOARD PRESENTATION

OCTOBER 10, 2023



DIGITAL SCOREBOARD 23-002

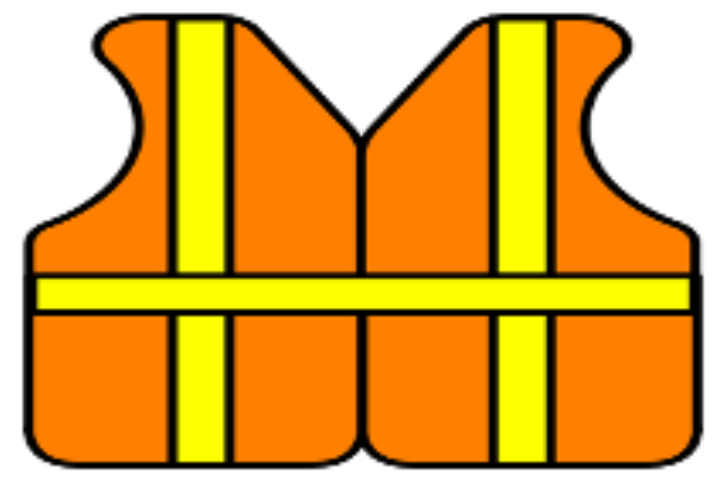

Digital Scoreboard 23-002 Closed 8/29/2023 10:00 AM		
	Daktronics	Major Display
Cost (ea)	\$239,051.84	\$187,687.00
Digital Speaker	\$54,070.00	\$17,490.00
Software	\$0.00	\$3,650.00
Track and Field Time	\$0.00	\$11,780.00
Arch Truss/Backlit Logos	\$6,192.00	\$8,252.00
Play Clocks	\$4,988.00	\$10,950.00
Rating	354	385
Total Cost (3 Each)	\$304,301.84	\$239,809.00
Total Cost	\$912,905.52	\$719,427.00
HKT	\$53,461.14	\$47,137.00
Grand Total	\$966,366.66	\$766,564.00
